

Statewide Orthoimagery Program


Coastal 2012

Eastern Piedmont 2013


Northern Piedmont and Mountains 2014

Geographic Information Coordinating Council

November 13, 2013



Statewide Digital Orthoimagery Acquisition Cycle

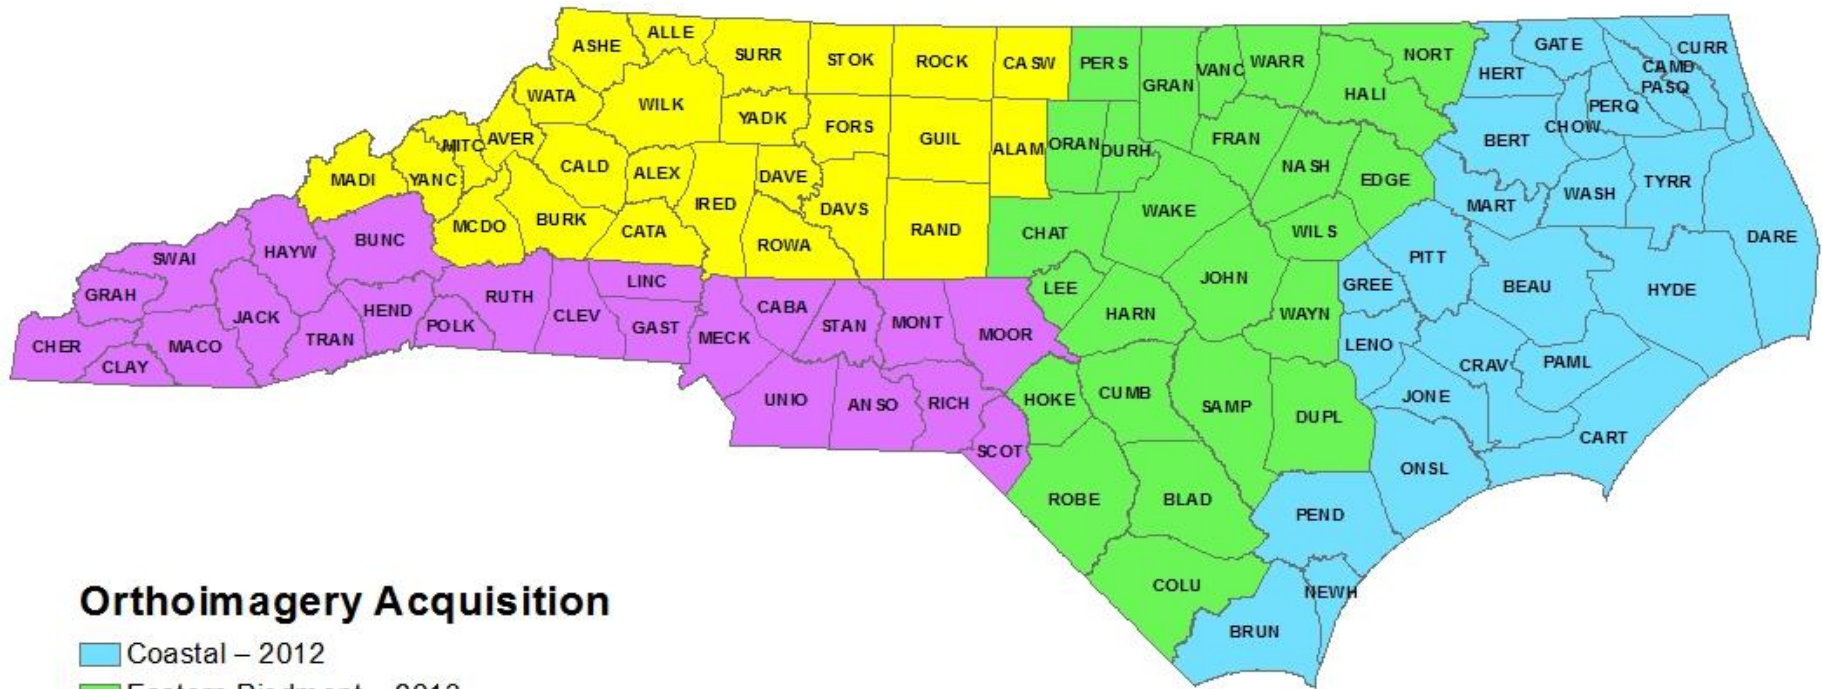

Orthoimagery Acquisition

- Coastal – 2012
- Eastern Piedmont – 2013
- Northern Piedmont and Mountains – 2014
- Southern Piedmont and Mountains – 2015

April 2013

Sources: NC Center for Geographic Information and Analysis and the Working Group for Orthophotography Planning
Statewide Mapping Advisory Committee


0 50 Miles



NCGICA

Coastal 2012 Summary

- Final Report submitted to NC 911 Board on Sep 26
 - 25 counties delivered on schedule and under budget
 - Cloud-based quality control tool facilitated efficient reporting of issues
 - Regular weekly project status meetings surfaced issues early for discussion/resolution
 - SharePoint enabled more efficient collaboration between contractors and state team
- Report will be posted on Statewide Orthoimagery Program website

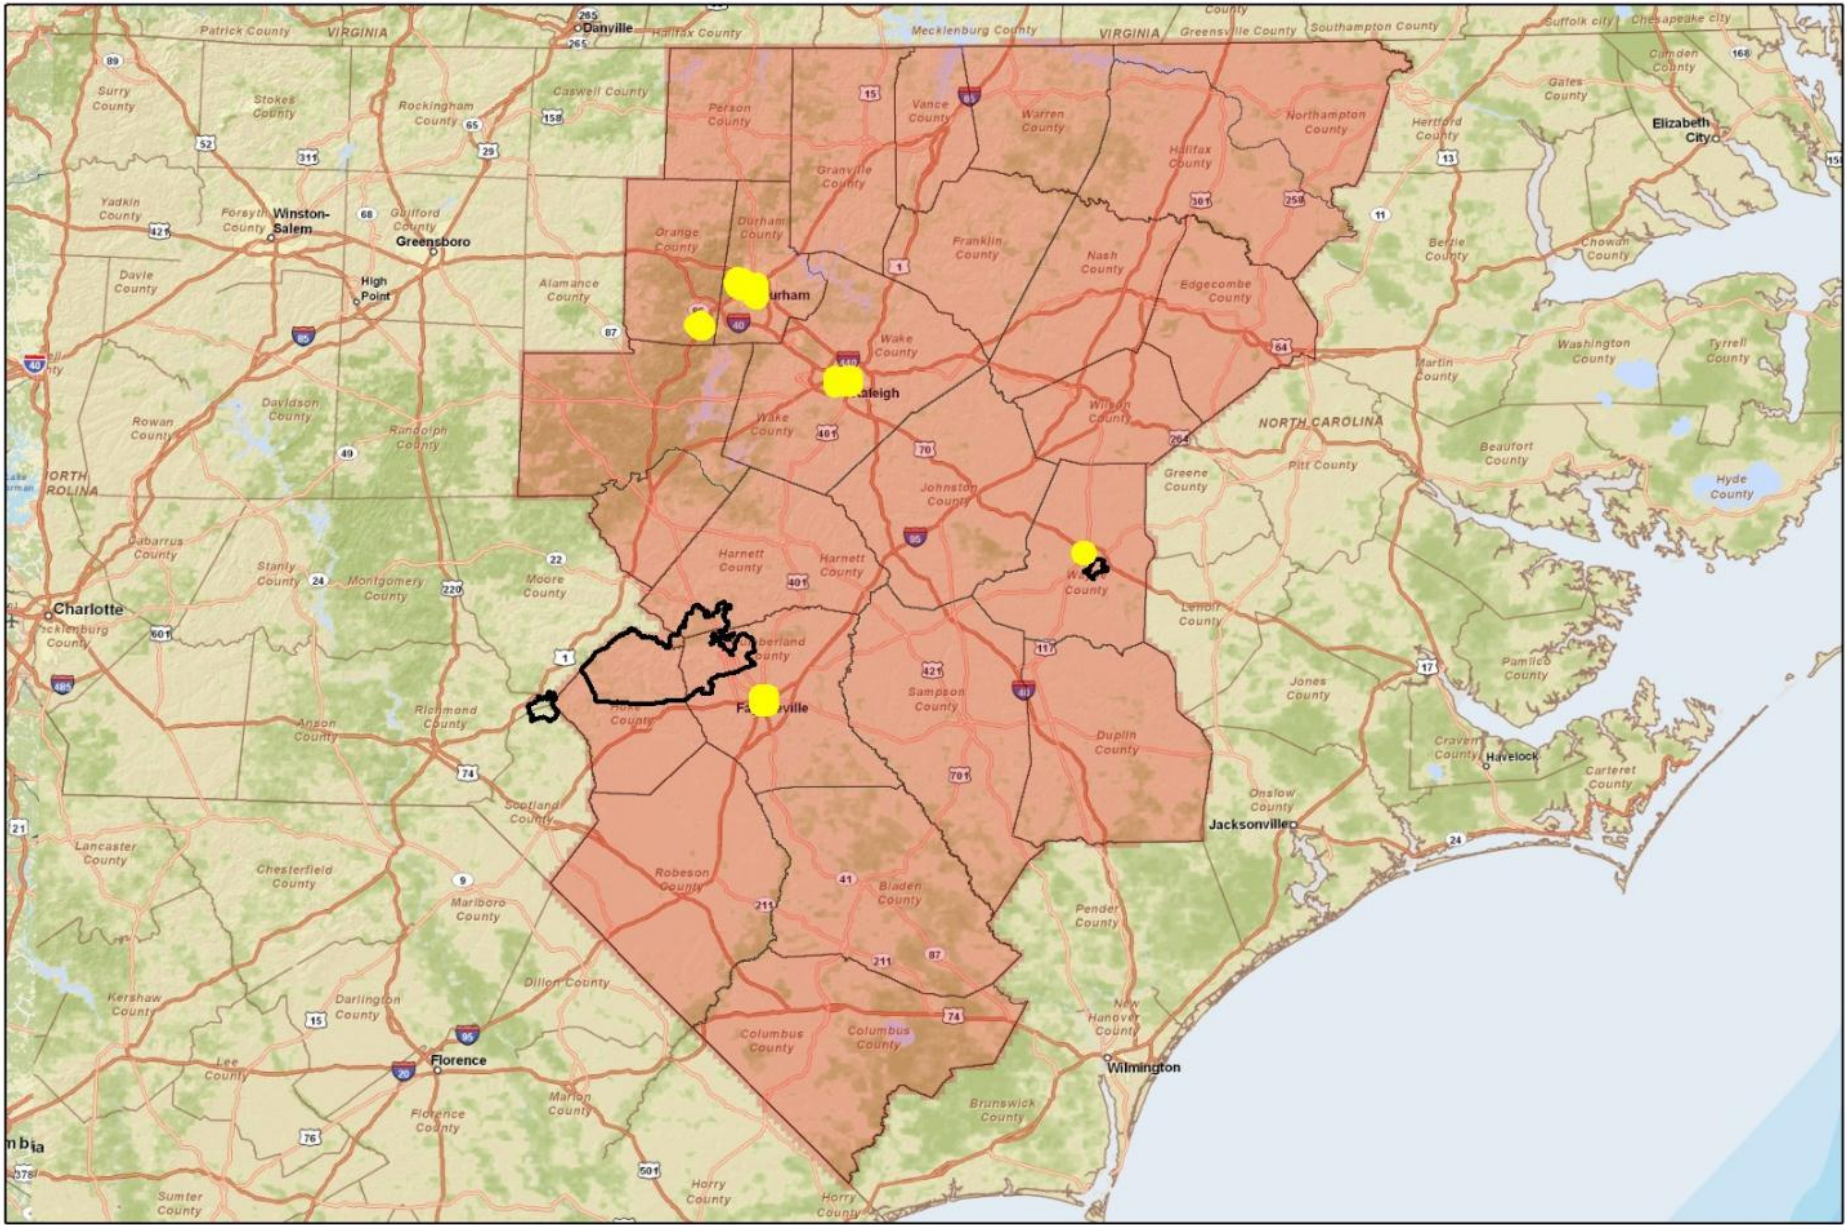

Eastern Piedmont 2013 Study Area

- NADIR Locations
- Military Installation
- Seymour Johnson Installation Boundary
- Study Area

0 20 Miles



Date: 11/15/2012




Eastern Piedmont 2013 Status

- Visual QC of all 25 counties complete
- Contractors have delivered sixteen counties to CGIA with all to be delivered by Dec 4
- Fort Bragg delivery and logistics in progress

Warren	Franklin	Vance	Wake
Wayne	Wilson	Nash	Edgecombe
Johnston	Harnett	Robeson	Cumberland
Sampson	Duplin	Bladen	Columbus

Eastern Piedmont 2013 VOICE

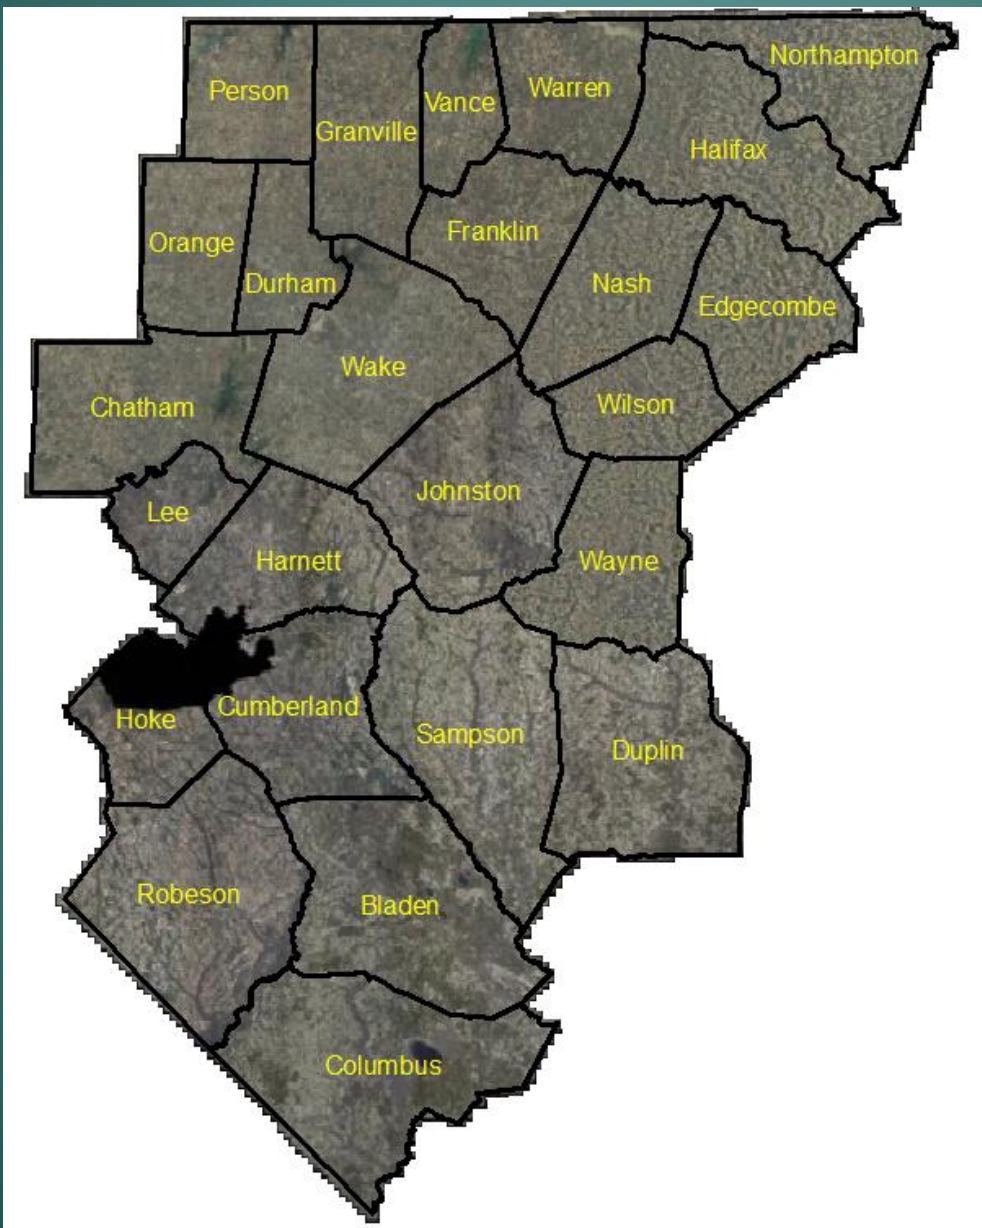


- 738 quality issues submitted to contractors

Eastern Piedmont 2013 Schedule


Date/Duration	Activity
Dec 19, 2012	Kickoff Meeting
Feb 1–Mar 31, 2013	Acquisition
Apr–Jul 2013	Post Processing and Outreach
Aug–Dec 2013	Quality Review Lifecycle
Jan 2014	Product Distribution Period
Feb–Mar 2014	User 60-Day Review Cycle



Product Distribution Meetings

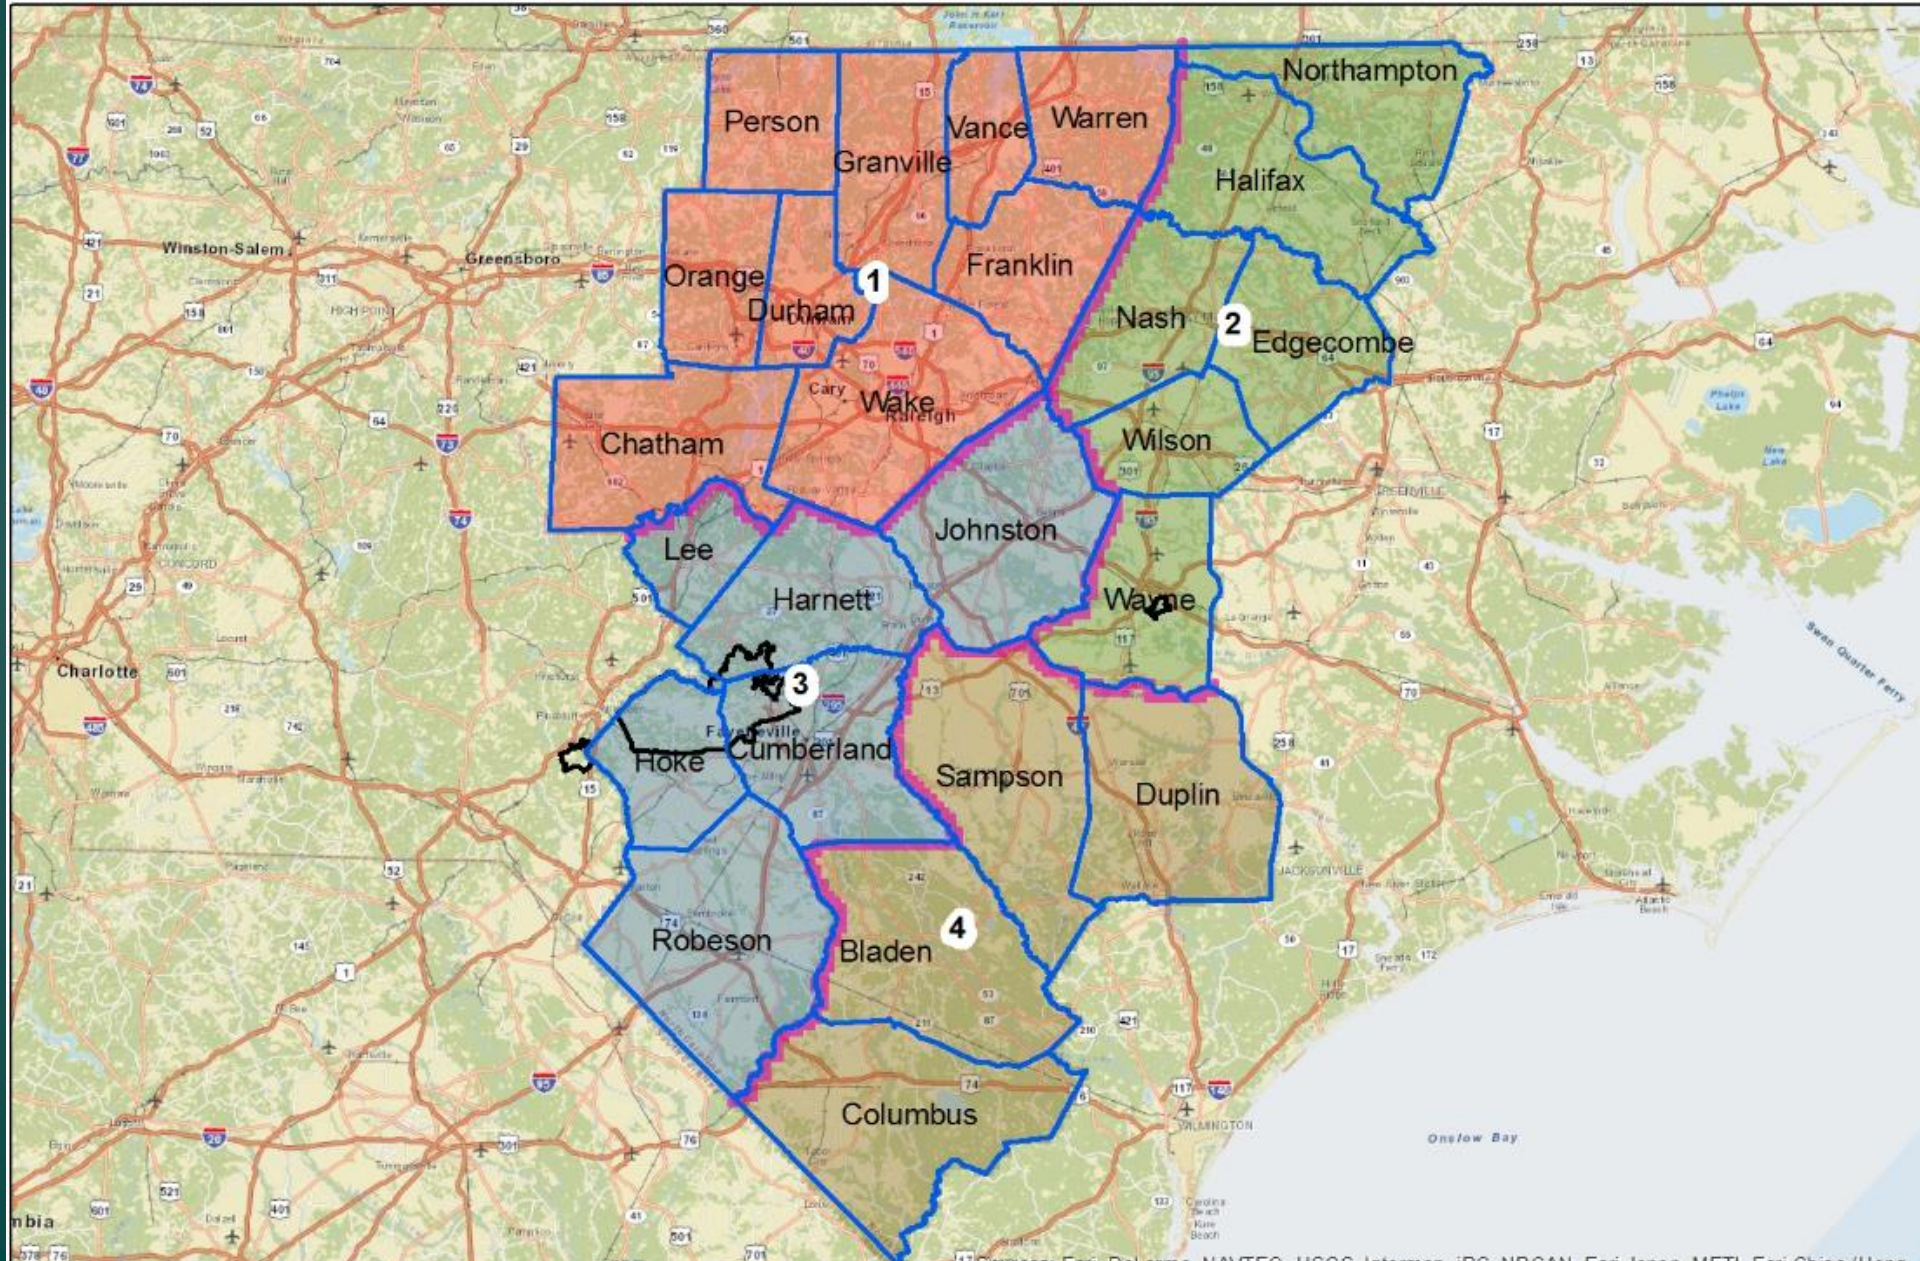

Northern Piedmont and Mountains

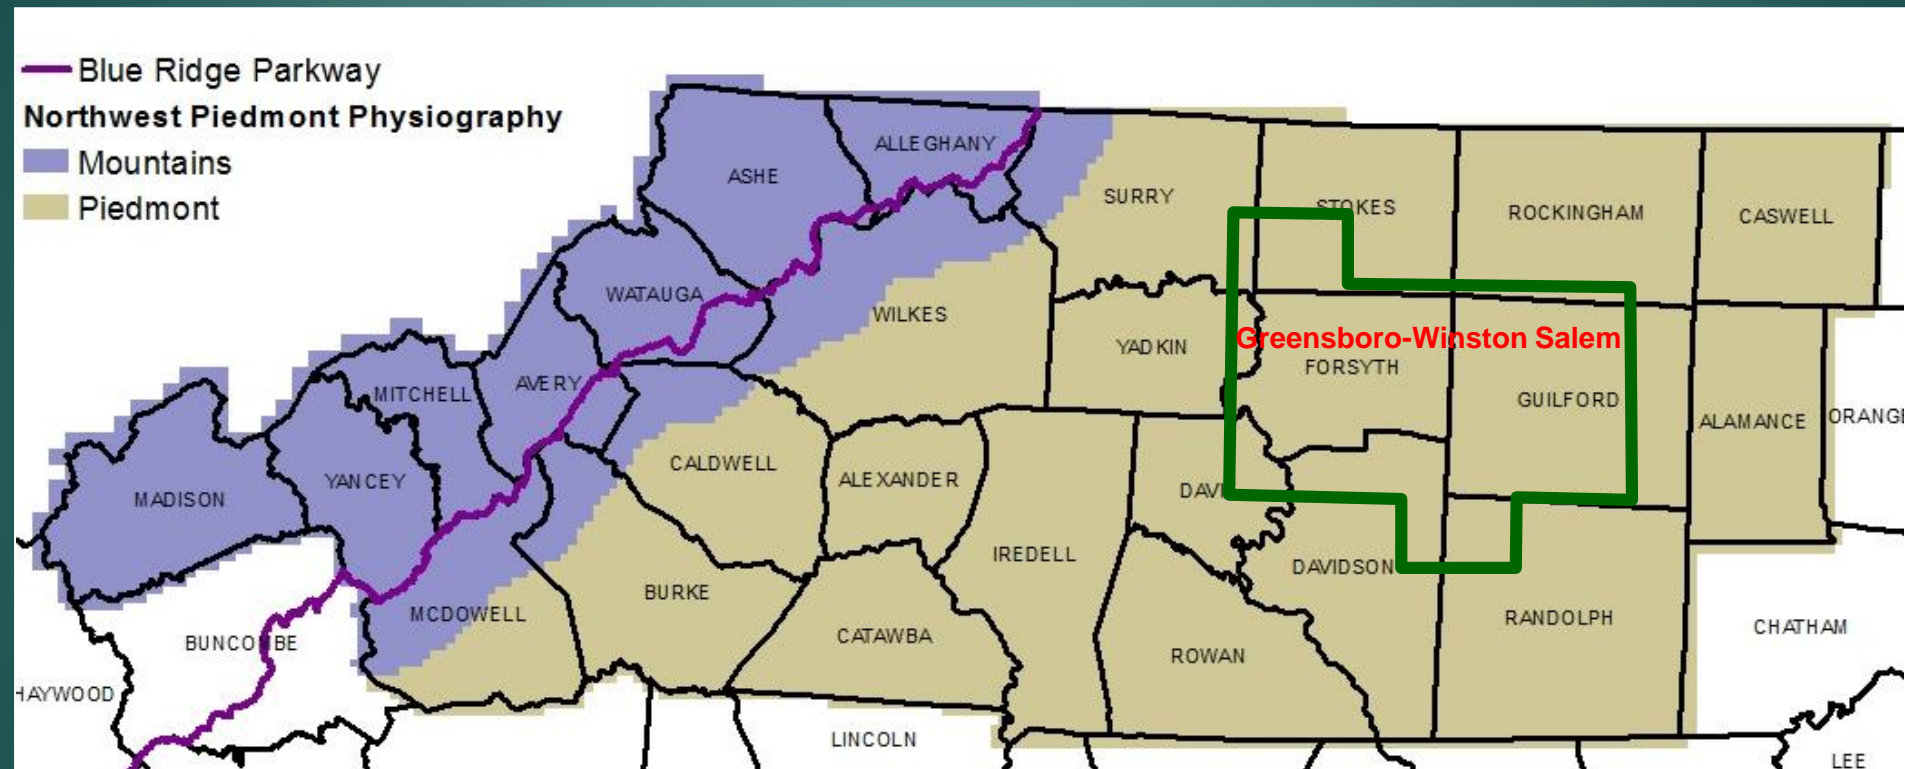

Northern Piedmont and Mtns 2014 Status

- Qualifications-Based Selection (QBS) process started
 - Request for Qualifications (RFQ) released on Sep 5
 - Bid Open occurred on Sep 25
- Project team completed evaluation of responses
- List of five selected respondents published on Oct 18
- Pre-Proposal meeting held on Nov 5

Northern Piedmont and Mtns 2014

Date/Duration	Activity
Sep 2013	QBS Period
Sep 2013-Jan 2014	Project Planning, PSAP Outreach
Oct-Nov 2013	Evaluation of Responses and Selection of Contractors
Dec 2013	Contracting and Project Kickoff
Feb-Apr 2014	Imagery Flights



Questions?

Darrin Smith
Technical Project Manager
919.754.6589
darrin.smith@nc.gov

Tim Johnson
CGIA Director
919.754.6588
tim.johnson@nc.gov

www.ncgicc.org
www.nconemap.com

